


Brattleboro Memorial Hospital

Modernization Boiler Project

Construction Schedule REV 1 082418

ID	Task Name	Duration	Start	Finish	Predecessors	Jul '18	Aug '18	Sep '18	Oct '18	Nov '18	Dec '18	Jan '19	Feb '19	Mar '19	Apr '19	May '19	Jun '19	Jul '19
1	Construction Time Frame	204 days	Thu 8/30/18	Thu 6/13/19														
2	Phase 1 Install boilers NB #1&2	65 days	Thu 8/30/18	Fri 11/30/18														
3	Mobilize	1 day	Mon 9/10/18	Mon 9/10/18														
4	Breakdown / Demo / Remove XB #3/temp blow down	2 days	Tue 9/11/18	Wed 9/12/18	3													
5	Remove from building EB#3	1 day	Thu 9/13/18	Thu 9/13/18	4													
6	Layout / Prep / Pour new HK Pad for NB #1&2	2 days	Fri 9/14/18	Mon 9/17/18	5													
7	All boilers delivered to Riggers	1 day	Thu 8/30/18	Thu 8/30/18														
8	Clean Oil Tank #2	3 days	Mon 9/10/18	Wed 9/12/18														
9	Breakdown new boilers @ Riggers to allow them to get into building	5 days	Tue 9/4/18	Mon 9/10/18	7FS+1 day													
10	Transport NB #1 & 2 to site	1 day	Thu 9/20/18	Thu 9/20/18	6FS+2 days													
11	Install NB #1&2 on HK pads	1 day	Fri 9/21/18	Fri 9/21/18	10													
12	Blake install parts back on boilers NB #1&2	3 days	Mon 9/24/18	Wed 9/26/18	11													
13	New interior boiler piping and fuel system boiler NB #1&2	25 days	Mon 9/24/18	Mon 10/29/18	11													
14	New interior duct work and breaching	25 days	Mon 9/24/18	Mon 10/29/18	11													
15	Electrical rough in	25 days	Mon 9/24/18	Mon 10/29/18	11													
16	ATC rough in	25 days	Mon 9/24/18	Mon 10/29/18	11													
17	Prep exterior louver openings for new work	4 days	Tue 9/18/18	Fri 9/21/18	6													
18	Install new louvers	1 day	Tue 10/30/18	Tue 10/30/18	14													
19	Rework Mezanine	3 days	Wed 10/31/18	Fri 11/2/18	18													
20	Surge tank and Fuel pump set installation	10 days	Fri 11/9/18	Thu 11/22/18	19FS+4 days													
21	Start/test/commision NB #1&2	4 days	Fri 11/23/18	Wed 11/28/18	20													

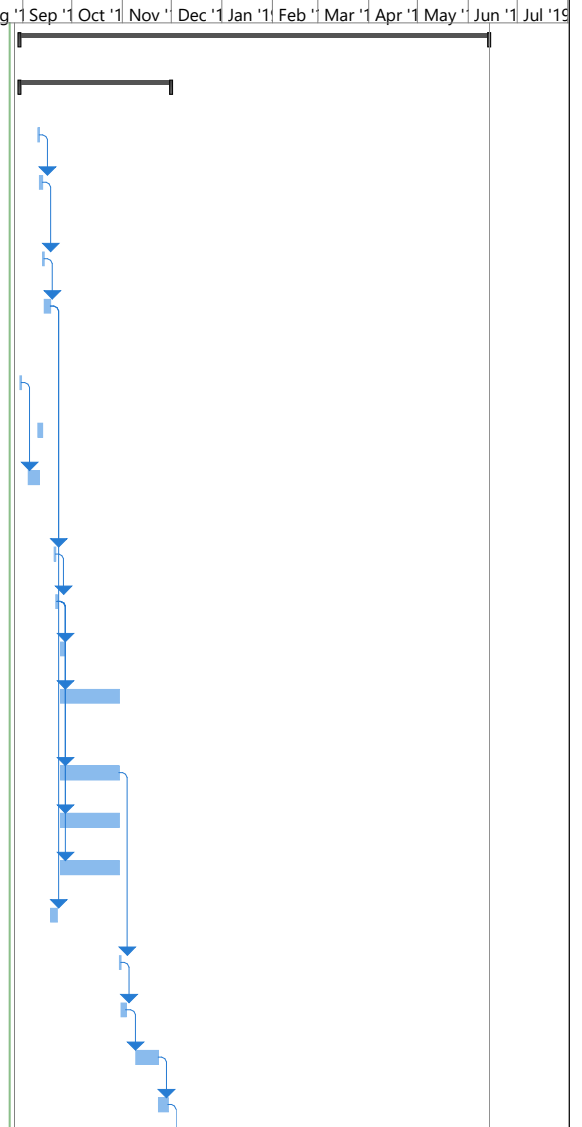

Brattleboro Memorial Hospital

Modernization Boiler Project

Construction Schedule REV 1 082418

ID	Task Name	Duration	Start	Finish	Predecessors	Jul '18	Aug '18	Sep '18	Oct '18	Nov '18	Dec '18	Jan '19	Feb '19	Mar '19	Apr '19	May '19	Jun '19	Jul '19	
22	Boiler inspection	1 day	Thu 11/29/18	Thu 11/29/18	21														
23	NB #1&2 complete and running	1 day	Fri 11/30/18	Fri 11/30/18	22														
24	Phase 2 Install boilers NB #3&4	59 days	Mon 3/25/19	Thu 6/13/19															
25	Shut down existing boilers #1&2	1 day	Mon 3/25/19	Mon 3/25/19															
26	Breakdown / Demo / Remove XB #1&2	5 days	Tue 3/26/19	Mon 4/1/19	25														
27	Layout / Prep / Pour new HK Pad for NB #3, 4 & (5?)	5 days	Tue 4/2/19	Mon 4/8/19	26														
28	Transport NB #3 & 4 to site	1 day	Tue 4/9/19	Tue 4/9/19	27														
29	Install NB #3&4 on HK pads	2 days	Wed 4/10/19	Thu 4/11/19	28														
30	Blake install parts back on boilers NB #3&4	3 days	Fri 4/12/19	Tue 4/16/19	29														
31	Install new exterior door frame	2 days	Fri 4/12/19	Mon 4/15/19	29														
32	Clean fuel tank #1	3 days	Wed 4/17/19	Fri 4/19/19	30														
33	New interior boiler piping and fuel system boiler NB #3&4	25 days	Wed 4/17/19	Tue 5/21/19	30														
34	New breaching	25 days	Wed 4/17/19	Tue 5/21/19	30														
35	Electrical rough in	25 days	Wed 4/17/19	Tue 5/21/19	30														
36	ATC rough in	25 days	Wed 4/17/19	Tue 5/21/19	30														
37	Start/test/commission NB #1&2	4 days	Wed 5/22/19	Mon 5/27/19	33														
38	Boiler inspection	1 day	Tue 5/28/19	Tue 5/28/19	37														
39	NB #1&2 complete and running	1 day	Wed 5/29/19	Wed 5/29/19	38														
40	Epoxy flooring	10 days	Thu 5/30/19	Wed 6/12/19	39														
41	Paint	25 days	Wed 4/17/19	Tue 5/21/19	34SS														
42	Project completed	1 day	Thu 6/13/19	Thu 6/13/19	40														

